ZINC ORE SERVICE

CLASS LO Nos 1 TO 8

CAPY. POUNDS -	140000#	
ESTIMATED CAPY.	CUBIC FEET TO SIDE PL.	TO ROOF PONY
CENTER COMPT	244	262
ONE END "	393	432
TWO END "	788	868
TOTAL CAR "	1050	1186

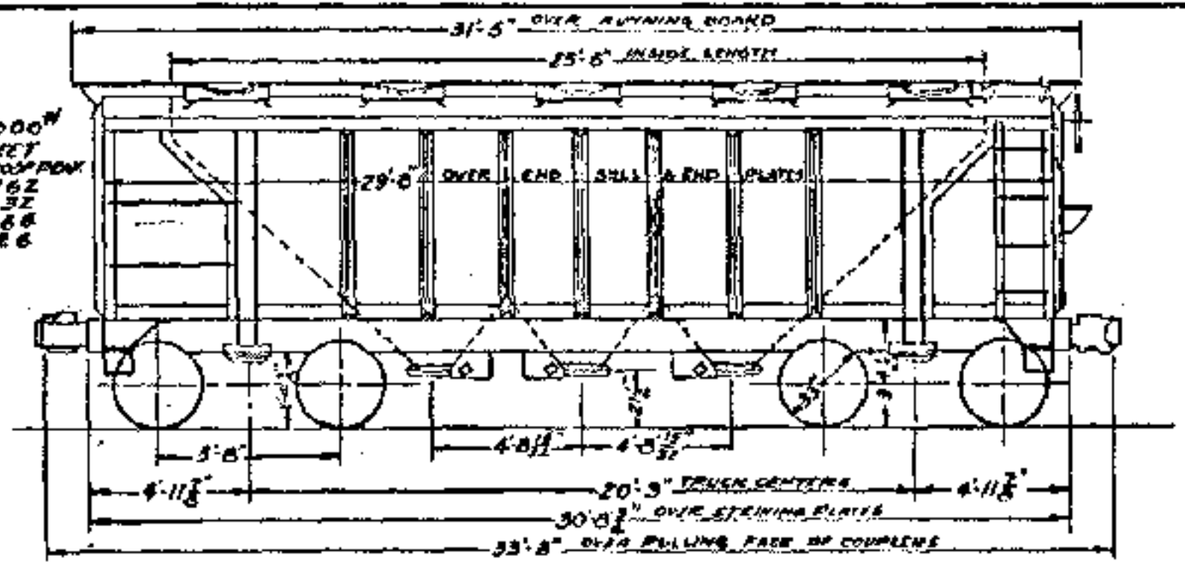

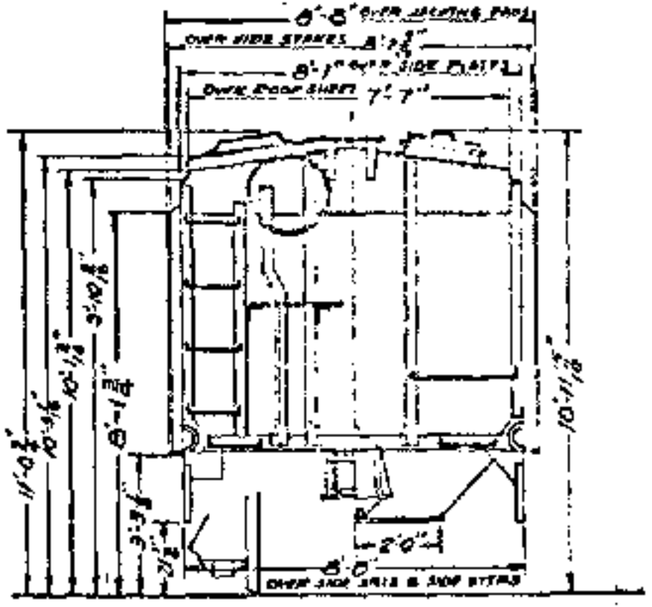

BUILDER-	C.R.R. of N.J.	SIDE SILL -	6"x4"x3/8" L	COUPLER -	AAR-6 1/2"x8" TYPE-E	JOURNALS -	6"x11"
BUILT -	1948	BODY BOLSTER -	24"x76" I	HOPPER -	ENTERPRISE	SIDE BEARING -	STUCKI ROLLER
WEIGHT - 47400 lbs.	CAPY - SEE ABOVE	SUPERSTRUCTURE -	STEEL	HAND BRAKE -	MINER	TRUCK SNUBBER -	SYM-GOULD CORP.
INSIDE LENGTH -	25'-6"	ROOF -	R.R. CO STEEL	BRAKE -	W.A.B. CO. AB 1012	RUNNING BOARD	APEX
INSIDE WIDTH -	8'-0"	HATCHES - MAIN -	10 - 28"x28"	BRAKE REGULATOR -	ROYAL TYPE-K		
UNDERFRAME -	STEEL	" SUPP. -	10 - 18" DIA.	SIDE FR & BOLSTER -	CAST STEEL		
CENTER SILL -	2-AAR 12 3/4"x38.7" I	DRAW GEAR	HULSON No 20E	WHEELS -	M.W. WROT STEEL		
